

BRUHAT BANGALORE MAHANAGARA PALIKE									
Name of work: Improvements to roads and drains at western side of Hegdenagara 2nd main road from 1st cross to 7th cross and surrounding Areas in Ward No.06									
Measurement Sheet									
First and Final Bill									
Item No:	1								
Item Name:	KSRRB300 - Excavation for road, drains and similar works, KSRRB300-1 : Earthwork excavation by manual means in ordinary soil involving as average horizontal throw upto 2 mtrs and an average lifts upto 0.5m, excavated surface leveled and sides neatly dressed, the disposed earth to be leveled neatly after breaking of clods complete as per specifications with all lead and lift and as per the direction of Engineer in-charge.								
SLNO	CHAINAGE	NO	L	B	D	QTY	REMARKS	RATE	AMOUNT
	Land Mark		(m)	(m)	(m)				
						1810.60			
	Vide Premeasurement Page no. 1 to 3					1810.60	Cum	226.00	409196.05
	Qty Payable in this bill								
Item No:	2								
Item Name:	KSRB M2100-10 : Providing and laying plain cement concrete of Mix 1:3:6 with OPC @ 220kgs, with crushed 40mm and down size graded granite mental coarse aggregate @ 0.89 cum and fine aggregate @ 0.46 cum, in foundation mechanically mixed, placed in foundation and compacted by vibration including curing for 14 days including cost of all material, labour, HOM curing, form work, scaffolding and centering complete as per specifications. Qty Upto 125%								
SLNO	CHAINAGE	NO	L	B	D	QTY	REMARKS	RATE	AMOUNT
	Land Mark		(m)	(m)	(m)				
						552.04			
	Vide Premeasurement Page no. 4 to 6					518.25			
						33.79			
	Qty Payable in this bill					552.04	Cum	5691.91	3142169.11
Item No:	3								
Item Name:	Providing and laying plain/reinforced cement concrete for side drains using M20 nominal mix concrete with OPC at 300 kgs. with 20mm and down size granite metal coarse aggregates at 0.69 cum and fine aggregates at 0.43 cum machine mixed, well compacted for walls and bottom including centering, shuttering, cost of materials, HOM of machinery, curing etc., complete excluding cost of steel as per MORTH specification No. 1500, 1700, 2200. including cost of materials, labour, HOM complete as per specifications. Page No.270. Item No.37.59.1								
SLNO	CHAINAGE	NO	L	B	D	QTY	REMARKS	RATE	AMOUNT
	Land Mark		(m)	(m)	(m)				
						529.83			
	Vide Premeasurement Page no. 5 to 10					529.83	Cum	7422.30	3932557.21
	Qty Payable in this bill								

K.S. Chowdary
Contractor Representative

Consultant Representative

[Signature]
Asst Engineer 30/11/2021

[Signature]
Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Item No:	4										127
Item Name:	KSRRB M 2200-6 Providing T.M.T steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and or welding wherever required, tying with binding wire and anchoring to the adjoining members wherever necessary complete as per design (laps, hooks and wastage shall not be measured and paid) cost of materials, labour, HOM of machinery complete as per specifications. Specification No. MORTH Specification No 1600 & 2200 TMT Bars Fe 500 Page No 229 Item No 28.8.2 SR 2018-19										
SLNO	CHAINAGE	NO	L	B	D	QTY	REMARKS	RATE	AMOUNT		
	Land Mark		(m)	(m)	(m)						
	Vide Premeasurement Page no. 11 + 12					40.23 ✓					
	Qty Payable in this bill					40.23 ✓	Tonne	77677.05	3125125.61		
Item No:	9										
Item Name:	KSRRB 4-1.6: Providing and laying in position plain cement concrete of Mix 1:2:4 with OPC at 240kgs, with 20mm and down size granite metal coarse aggregates at 0.878 cum and fine aggregates at 0.53cum, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted in foundation, plinth and cills, including cost of materials, labours, HOM curing complete as per specifications. specifications No. KBS 4.1,4.2.(P.No-13, I.No4.6)										
SLNO	CHAINAGE	NO	L	B	D	QTY	REMARKS	RATE	AMOUNT		
	Land Mark		(m)	(m)	(m)						
	Vide Premeasurement Page no. 15 + 14					42.89 ✓					
	Qty Payable in this bill					42.89 ✓	Cum	6033.54	258778.53		
Item No:	E-1										
Item Name:	KSRRB M300-14. Excavation for roadwork in soil with hydraulic excavator of 0.9 cum bucket capacity including cutting and loading in tippers, trimming bottom and side slopes, in accordance with requirements of lines, grades and cross sections, and transporting to the embankment location to a lead of 1km and complete as per specifications.(I No-19.14,P No-143).										
SLNO	CHAINAGE	NO	L	B	D	QTY	REMARKS	RATE	AMOUNT		
	Land Mark		(m)	(m)	(m)						
	Vide Premeasurement Page no. 15					735.81 ✓					
	Qty Payable in this bill					735.81 ✓	Cum	45.62	33571.00		

K. S. Chowdareddy
Contractor Representative

Consultant Representative

Asst Engineer 30/4/21

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

20

Item No:	E-2								
Item Name:	KSRRB 300-58, Compaction of original ground by mechanical means including filling in depression occurring during rolling including cost of all labour, HOM complete as per specifications.(I No-19.64,P No-147)								
SLNO	CHAINAGE	NO	L	B	D	QTY	REMARKS	RATE	AMOUNT
	Land Mark		(m)	(m)	(m)				
Vide Premeasurement Page no. (16)						1839.54			
Qty Payable in this bill						1839.54	Sqm	6.68	12282.07
Item No:	E-3								
Item Name:	Construction of granular sub-base Grading-V as Sub-base and drainage layer by providing coarse graded crushed stone aggregates of granite/ trap/basalt material, mixing in a mechanical mix plant at OMC, Carriage of mixed material to work site, spreading in uniform layers with motor grader on prepared surface and compacting with vibratory power roller to achieve the 98 % proctor density, complete as per specifications Clause 401 of MORTH V Revision.(I No-20.5,P No-153)								
SLNO	CHAINAGE	NO	L	B	D	QTY	REMARKS	RATE	AMOUNT
	Land Mark		(m)	(m)	(m)				
Vide Premeasurement Page no. (17)						368.25			
Qty Payable in this bill						368.25	Cum	2094.27	771212.78

K. S. Chowdareddy
Contractor Representative

ARTIN ASSOCIATES
CONSULTANTS
BANGALORE
Consultant Representative

Asst Engineer 30/11/21

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92
30/11/21

BRUHAT BANGALORE MAHANAGARA PALIKE											
Name of work: Improvements to roads and drains at western side of Hegdenagara 2nd main road from 1st cross to 7th cross and surrounding Areas in Ward No.06											
Measurement Sheet											
First and Final Bill											
Item No:	5										
Item Name:	Providing and Fixing RCC pre cast covering Slab of 100mm thick for drains in cement concrete M25 using graded granite jelly 20mm and down size with steel reinforcement , including form work, lift charges, curing and concrete finished surfaces on both side etc., complete as per drawing and the directions of Engineer in-charge.(Date rate)										
Premeasurement recorded on:											
SLNO	CHAINAGE	NO	L	B	B1	Avg B	D	QTY	REMARKS	RATE	AMOUNT
	Land Mark		(m)	(m)	(m)	(m)	(m)				
For New Drain											
5th cross road LHS (1st Main to 2nd Main)											
	0.00	30.00	1	30.00	0.90			27.00			
	30.00	60.00	1	30.00	0.90			27.00			
	60.00	90.00	1	30.00	0.90			27.00			
	90.00	120.00	1	30.00	0.90			27.00			
	120.00	150.00	1	30.00	0.90			27.00			
	150.00	180.00	1	30.00	0.90			27.00			
	180.00	190.00	1	10.00	0.90			9.00			
6th cross road LHS (2nd Main to 3rd Main)											
	0.00	30.00	1	30.00	0.90			27.00			
	30.00	60.00	1	30.00	0.90			27.00			
	60.00	90.00	1	30.00	0.90			27.00			
	90.00	120.00	1	30.00	0.90			27.00			
	120.00	150.00	1	30.00	0.90			27.00			
	150.00	180.00	1	30.00	0.90			27.00			
	180.00	210.00	1	30.00	0.90			27.00			
	210.00	221.00	1	11.00	0.90			9.90			
6th cross road RHS (2nd Main to 3rd Main)											
	0.00	30.00	1	30.00	0.90			27.00			
	30.00	60.00	1	30.00	0.90			27.00			
	60.00	90.00	1	30.00	0.90			27.00			
	90.00	120.00	1	30.00	0.90			27.00			
	120.00	150.00	1	30.00	0.90			27.00			
	150.00	180.00	1	30.00	0.90			27.00			
	180.00	210.00	1	30.00	0.90			27.00			
	210.00	221.00	1	11.00	0.90			9.90			
RK Hegdenagar 7th Main LHS											
7th cross road LHS (2nd Main to 3rd Main)											
	0.00	30.00	1	30.00	0.90			27.00			
	30.00	60.00	1	30.00	0.90			27.00			
	60.00	90.00	1	30.00	0.90			27.00			
	90.00	120.00	1	30.00	0.90			27.00			
	120.00	150.00	1	30.00	0.90			27.00			
	150.00	180.00	1	30.00	0.90			27.00			
	180.00	210.00	1	30.00	0.90			27.00			
	210.00	226.00	1	16.00	0.90			14.40			
7th cross road RHS (2nd Main to 3rd Main)											
	0.00	30.00	1	30.00	0.90			27.00			
	30.00	60.00	1	30.00	0.90			27.00			
	60.00	68.00	1	8.00	0.90			7.20			
	68.00	74.00	1	6.00							
	74.00	104.00	1	30.00	0.90			27.00			
	104.00	116.00	1	12.00	0.90			10.80			
	116.00	121.00	1	5.00							
	121.00	151.00	1	30.00	0.90			27.00			
	151.00	159.50	1	8.50	0.90			7.65			

[Signature]
AE
30/11/21

[Signature]
Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92
30/11/21

SLNO	CHAINAGE		NO	L	B	B1	Avg B	D	QTY	REMARKS	RATE	AMOUNT
	Land Mark			(m)	(m)	(m)	(m)	(m)				
	159.50	164.50	1	5.00								
	164.50	194.50	1	30.00	0.90				27.00	culvert		
	194.50	210.00	1	15.50	0.90				13.95			
7th cross road LHS (1st Main to 2nd Main)												
	0.00	30.00	1	30.00	0.90				27.00			
	30.00	60.00	1	30.00	0.90				27.00			
	60.00	90.00	1	30.00	0.90				27.00			
	90.00	120.00	1	30.00	0.90				27.00			
	120.00	150.00	1	30.00	0.90				27.00			
	150.00	180.00	1	30.00	0.90				27.00			
	180.00	206.00	1	30.00	0.90				27.00			
			1	26.00	0.90				23.40			
7th cross road RHS (1st Main to 2nd Main)												
	0.00	30.00	1	30.00	0.90				27.00			
	30.00	60.00	1	30.00	0.90				27.00			
	60.00	90.00	1	30.00	0.90				27.00			
	90.00	120.00	1	30.00	0.90				27.00			
	120.00	150.00	1	30.00	0.90				27.00			
	150.00	180.00	1	30.00	0.90				27.00			
	180.00	206.00	1	30.00	0.90				27.00			
			1	26.00	0.90				23.40			
	Slab in 13th cross		26	0.60	0.90				14.04			
Total Qty Work Done									1331.64	Sqm		
Qty Payable in this bill									1331.64	Sqm	2453.38	3267018.94

Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore-92

K.S. Chowdary
Contractor Representative
30/11/21

Consultant Representative

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

25

BRUHAT BANGALORE MAHANAGARA PALIKE

Name of work: Improvements to roads and drains at western side of Hegdenagara 2nd main road from 1st cross to 7th cross and surrounding Areas in Ward No.06

Measurement Sheet
First and Final Bill

Item No: 8

Item Name: Providing and Fixing pre cast covering Slab 250mm thick made out of M25 and jelly 20mm Down size with steel reinforcement including form work, curing, including cost of all materials, labour, hire charges of machinery, loading, unloading, lead and lift, transportation etc, complete. As per Engineer incharge.

Premeasurement recorded on:

SLNO	CHAINAGE		NO	L	B	BI	Avg B	D	QTY	REMARKS	RATE	AMOUNT
	Land Mark			(m)	(m)	(m)	(m)	(m)				
	Culverts											
	5th cross road culvert											
	0.00	9.30	1	9.30	1.50				13.95			
	7th cross road culvert											
	0.00	6.80	1	6.80	1.50				10.20			
	7th cross road RHS (2nd Main to 3rd Main)											
	68.00	74.00	1	6.00	1.50				9.00			
	116.00	121.00	1	5.00	1.50				7.50			
	159.50	164.50	1	5.00	1.50				7.50			
	Total Qty Work Done								48.15	Sqm		
	Qty Upto 125%								41.25			
	Qty Above 125%								6.90			
	Qty Payable in this bill								48.15	Sqm	5687.82	273868.53

K.S. Chowdareddy
Contractor Representative

K. Sundresh
Asst Engineer 30/11/21

[Signature]
Consultant Representative

[Signature]
Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

BRUHAT BANGALORE MAHANAGARA PALIKE

Name of work: Improvements to roads and drains at western side of Hegdenagar 2nd main road from 1st cross to 7th cross and surrounding Areas in Ward No.06

Measurement Sheet
First and Final Bill

Item No. 10
Item Name: Providing and fixing pre cast solid cement concrete kerb stones made out of CC 1:2:4 with top and bottom width 114 and 165 mm respectively, 400mm high and 450mm in length finished with CM 1:3 plastering and finishing cutting including formwork, curing, including cost of materials, labour charges of machinery.

Premasurement recorded on:

SLNO	CHAINAGE		NO	L	B	BI	Avg B	D	QTY	REMARKS	RATE	AMOUNT	
	Land Mark			(m)	(m)	(m)	(m)	(m)					
For New Drain													
5th cross road LHS (1st Main to 2nd Main)													
	0.00	30.00	1	30.00					30.00	}			
	30.00	60.00	1	30.00					30.00				
	60.00	90.00	1	30.00					30.00				
	90.00	120.00	1	30.00					30.00				
	120.00	150.00	1	30.00					30.00				
	150.00	180.00	1	30.00					30.00				
	180.00	190.00	1	10.00					10.00				
6th cross road LHS (2nd Main to 3rd Main)													
	0.00	30.00	1	30.00					30.00	}			
	30.00	60.00	1	30.00					30.00				
	60.00	90.00	1	30.00					30.00				
	90.00	120.00	1	30.00					30.00				
	120.00	150.00	1	30.00					30.00				
	150.00	180.00	1	30.00					30.00				
	180.00	210.00	1	30.00					30.00				
	210.00	221.00	1	11.00					11.00				
6th cross road RHS (2nd Main to 3rd Main)													
	0.00	30.00	1	30.00					30.00	}			
	30.00	60.00	1	30.00					30.00				
	60.00	90.00	1	30.00					30.00				
	90.00	120.00	1	30.00					30.00				
	120.00	150.00	1	30.00					30.00				
	150.00	180.00	1	30.00					30.00				
	180.00	210.00	1	30.00					30.00				
	210.00	221.00	1	11.00					11.00				
RK Hegdenagar 7th Main LHS													
7th cross road LHS (2nd Main to 3rd Main)													
	0.00	30.00	1	30.00					30.00	}			
	30.00	60.00	1	30.00					30.00				
	60.00	90.00	1	30.00					30.00				
	90.00	120.00	1	30.00					30.00				
	120.00	150.00	1	30.00					30.00				
	150.00	180.00	1	30.00					30.00				
	180.00	210.00	1	30.00					30.00				
	210.00	226.00	1	16.00					16.00				
7th cross road RHS (2nd Main to 3rd Main)													
	0.00	30.00	1	30.00					30.00	}			
	30.00	60.00	1	30.00					30.00				
	60.00	68.00	1	8.00					8.00				
	68.00	74.00	1	6.00							culvert		
	74.00	104.00	1	30.00					30.00				
	104.00	116.00	1	12.00					12.00				
	116.00	121.00	1	5.00						culvert			
	121.00	151.00	1	30.00					30.00				
	151.00	159.50	1	8.50					8.50				
	159.50	164.50	1	5.00						culvert			
	164.50	194.50	1	30.00					30.00				

Mudrey
Ae

Consultant Representative

Asst. Executive Engineer

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

92

Bruhat Bangalore Mahanagara Palike										
Name of work: Improvements to roads and drains at western side of Hegdenagara 2nd main road from 1st cross to 7th cross and surrounding Areas in Ward No.06										
MEASUREMENT										
Sl No	Description of Item	No	L	B1	B2	Av.B	D	Qty	Rate	Amount
E-4	Constructing un-reinforced, plain cement concrete for pavements using Grade concrete M30 over a prepared base with OPC coarse aggregate at 0.69 cum, fine aggregates at 0.46 cum, Coarse and fine aggregate conforming to IS:383-2016, with Superplastizer at 3 lts conforming to IS 9103-2008. mixed in a concrete mixer of not less than 0.6 cum capacity and appropriate weigh batcher as per approved mix design, laid in approved fixed side form work (steel channel, laying and fixing of 125 micron thick polythene film, wedges, steel plates including levelling the form work as per drawing). & Spreading the concrete with shovels, rakers compacted using needle, screed and plate vibrator and finished with floaters in a continuous operation including provision of contraction, expansion, construction and longitudinal joints, including groove cutting charges, joint filler, separation membrane of impermeable plastic sheet of 125 micron, sealant primer, joint sealant, admixtures as approved, curing compound, finishing to -do- with OPC at 360 kg/cum and coarse aggregate 0.69cum, fine aggregate 0.46cum.									
	C C Road								CUM	
	Cross Road 1									
	Ch: 0.00 to 15.00 Mts	1.00	15.00	4.90	4.60	4.75	0.15	10.69		
	Ch: 15.00 to 30.00 Mts	1.00	15.00	4.60	4.60	4.60	0.15	10.35		
	Ch: 30.00 to 45.00 Mts	1.00	15.00	4.60	4.75	4.68	0.15	10.52		
	Ch: 45.00 to 60.00 Mts	1.00	15.00	4.50	4.50	4.50	0.15	10.13		
	Ch: 60.00 to 75.00 Mts	1.00	15.00	4.60	4.56	4.58	0.15	10.31		
	Ch: 75.00 to 90.00 Mts	1.00	15.00	4.56	4.60	4.58	0.15	10.31		
	Ch: 90.00 to 97.0 Mts	1.00	7.00	4.60	4.70	4.65	0.15	4.88		
	Cross Road 2									
	Ch: 0.00 to 15.00 Mts	1.00	15.00	6.00	5.95	5.98	0.15	13.44		
	Ch: 15.00 to 30.00 Mts	1.00	15.00	5.95	4.80	5.38	0.15	12.09		
	Ch: 30.00 to 45.00 Mts	1.00	15.00	4.80	4.75	4.78	0.15	10.74		
	Ch: 45.00 to 60.00 Mts	1.00	15.00	4.80	4.70	4.75	0.15	10.69		
	Ch: 60.00 to 75.00 Mts	1.00	15.00	4.60	4.60	4.60	0.15	10.35		
	Ch: 75.00 to 90.00 Mts	1.00	15.00	4.75	4.85	4.80	0.15	10.80		
	Ch: 90.00 to 94.0 Mts	1.00	4.00	4.85	4.90	4.88	0.15	2.93		
	DEDUCTION									
	Chamber	-2.00	0.90	0.90	-0.90	0.90	0.15	-0.24		
	Cross Road 3									
	Ch: 0.00 to 15.00 Mts	1.00	15.00	4.90	4.85	4.88	0.15	10.97		
	Ch: 15.00 to 30.00 Mts	1.00	15.00	4.85	4.75	4.80	0.15	10.80		
	Ch: 30.00 to 45.00 Mts	1.00	15.00	4.75	4.90	4.83	0.15	10.86		
	Ch: 45.00 to 60.00 Mts	1.00	15.00	4.90	4.95	4.93	0.15	11.08		
	Ch: 60.00 to 75.00 Mts	1.00	15.00	4.95	5.00	4.98	0.15	11.19		
	Ch: 75.00 to 90.00 Mts	1.00	15.00	5.00	5.25	5.13	0.15	11.53		
	Ch: 90.00 to 92.0 Mts	1.00	2.00	5.25	6.50	5.88	0.15	1.76		
	DEDUCTION									
	Chamber	-4.00	0.90	0.90	0.90	0.90	0.15	-0.49		
	Paralle Rd to Main Rd									
	Ch: 0.00 to 15.00 Mts	1.00	15.00	7.10	6.95	7.03	0.15	15.81		
	Ch: 15.00 to 17.50 Mts	1.00	2.50	6.95	6.85	7.03	0.15	2.64		
	Ch: 17.50 to 19.00 Mts								Culvert	
	Ch: 19.00 to 34.00 Mts	1.00	15.00	6.85	6.90	6.88	0.15	15.47		
	Ch: 34.00 to 46.50 Mts	1.00	12.50	6.90	7.10	7.00	0.15	13.13		
	Ch: 46.50 to 48.00 Mts								Culvert	
	Ch: 48.00 to 63.00 Mts	1.00	15.00	7.10	6.92	7.01	0.15	15.77		
	Ch: 63.00 to 70.00 Mts	1.00	7.00	6.92	7.25	7.09	0.15	7.44		
	Present Qty							275.93		
	Qty paid in this bill							275.93	5470.47	1509466.79


K. S. Chollareddy
Contractor Representative

Asst Engineer
30/11/2021

Consultant Representative
Asst. Executive Engineer
Project Division
Velahanka Zone
BBMP, Bangalore - 92


BRUHAT BANGALORE MAHANAGAR PALIKE												
Name of work: Improvements to roads and drains at western side of Hegdenagara 2nd main road from 1st cross to 7th cross and surrounding Areas in Ward No.06												
Measurement Sheet												
First and Final Bill												
Item No:	11											
Item Name:	KSRRB 800-1. Painting two coats after filling the surface with synthetic enamel paint in approved shades on new plastered concrete surfaces, with materials, labour complete as per specifications. MORTH Chapter 8											
Measurement recorded on:												
SLNO	CHAINAGE		NO	L	B	BI	Avg B	D	QTY	REMARKS	RATE	AMOUNT
	Land Mark			(m)	(m)	(m)	(m)	(m)				
For New Drain												
5th cross road LHS (1st Main to 2nd Main)												
	0.00	30.00	1	30.00				0.40	12.00			
	30.00	60.00	1	30.00				0.40	12.00			
	60.00	90.00	1	30.00				0.40	12.00			
	90.00	120.00	1	30.00				0.40	12.00			
	120.00	150.00	1	30.00				0.40	12.00			
	150.00	180.00	1	30.00				0.40	12.00			
	180.00	190.00	1	10.00				0.40	4.00			
6th cross road LHS (2nd Main to 3rd Main)												
	0.00	30.00	1	30.00				0.40	12.00			
	30.00	60.00	1	30.00				0.40	12.00			
	60.00	90.00	1	30.00				0.40	12.00			
	90.00	120.00	1	30.00				0.40	12.00			
	120.00	150.00	1	30.00				0.40	12.00			
	150.00	180.00	1	30.00				0.40	12.00			
	180.00	210.00	1	30.00				0.40	12.00			
	210.00	221.00	1	11.00				0.40	4.40			
6th cross road RHS (2nd Main to 3rd Main)												
	0.00	30.00	1	30.00				0.40	12.00			
	30.00	60.00	1	30.00				0.40	12.00			
	60.00	90.00	1	30.00				0.40	12.00			
	90.00	120.00	1	30.00				0.40	12.00			
	120.00	150.00	1	30.00				0.40	12.00			
	150.00	180.00	1	30.00				0.40	12.00			
	180.00	210.00	1	30.00				0.40	12.00			
	210.00	221.00	1	11.00				0.40	4.40			
RK Hegdenagar 7th Main LHS												
7th cross road LHS (2nd Main to 3rd Main)												
	0.00	30.00	1	30.00				0.40	12.00			
	30.00	60.00	1	30.00				0.40	12.00			
	60.00	90.00	1	30.00				0.40	12.00			
	90.00	120.00	1	30.00				0.40	12.00			
	120.00	150.00	1	30.00				0.40	12.00			
	150.00	180.00	1	30.00				0.40	12.00			
	180.00	210.00	1	30.00				0.40	12.00			
	210.00	226.00	1	16.00				0.40	6.40			
7th cross road RHS (2nd Main to 3rd Main)												
	0.00	30.00	1	30.00				0.40	12.00			
	30.00	60.00	1	30.00				0.40	12.00			
	60.00	68.00	1	8.00				0.40	3.20			
	68.00	74.00	1	6.00						culvert		
	74.00	104.00	1	30.00				0.40	12.00			
	104.00	116.00	1	12.00				0.40	4.80			
	116.00	121.00	1	5.00						culvert		
	121.00	151.00	1	30.00				0.40	12.00			
	151.00	159.50	1	8.50				0.40	3.40			
	159.50	164.50	1	5.00						culvert		
	164.50	194.50	1	30.00				0.40	12.00			
	194.50	210.00	1	15.50				0.40	6.20			

Handwritten signature
AC

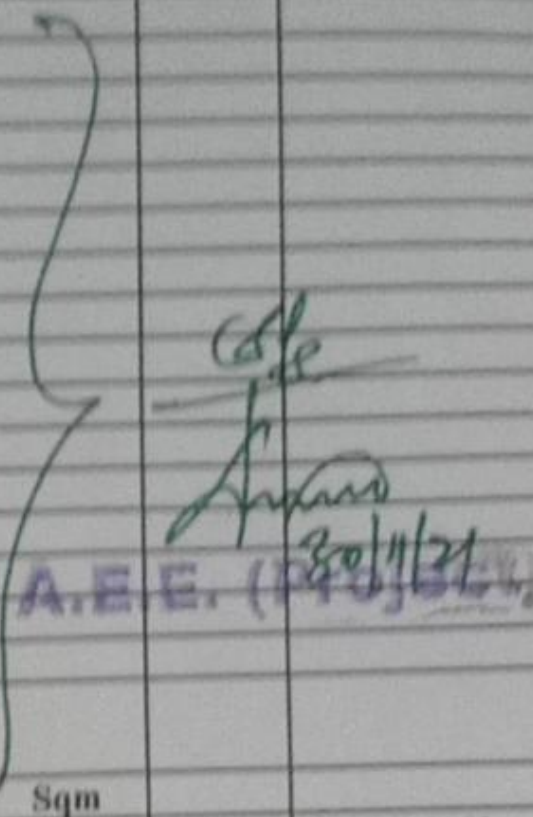SLNO	CHAINAGE		NO	L	B	BI	Avg B	D	QTY	REMARKS	RATE	AMOUNT
	Land Mark			(m)	(m)	(m)	(m)	(m)				
7th cross road LHS (1st Main to 2nd Main)												
	0.00	30.00	1	30.00				0.40	12.00			
	30.00	60.00	1	30.00				0.40	12.00			
	60.00	90.00	1	30.00				0.40	12.00			
	90.00	120.00	1	30.00				0.40	12.00			
	120.00	150.00	1	30.00				0.40	12.00			
	150.00	180.00	1	30.00				0.40	12.00			
	180.00	208.00	1	26.00				0.40	10.40			
7th cross road RHS (1st Main to 2nd Main)												
	0.00	30.00	1	30.00				0.40	12.00			
	30.00	60.00	1	30.00				0.40	12.00			
	60.00	90.00	1	30.00				0.40	12.00			
	90.00	120.00	1	30.00				0.40	12.00			
	120.00	150.00	1	30.00				0.40	12.00			
	150.00	180.00	1	30.00				0.40	12.00			
	180.00	208.00	1	26.00				0.40	10.40			
	Missing Kerb in 13th cross		5	3.00				0.40	6.00			
	Total Qty Work Done								591.60	Sqm		
	Qty Payable in this bill								591.60	Sqm	89.02	52664.23
Net amount												18279820.80
12% GST												2193578.50
Grand total												20473399.30

K.S. Chowdary
Contractor Representative

[Signature]
Asst Engineer 30/11/21



Consultant Representative

[Signature]
Asst. Executive Engineer
Project Division
Yeelahanka Zone
BBMP, Bangalore - 92
